



# BOND PROJECT UPDATES

(February 20, 2019)

## PROPOSITION 3 STREETS

### OLD GOFORTH ROAD IMPROVEMENT

The general scope of work for this project includes:

- Dedicated left and right turn lanes at Tom Green Elementary
  - Intersection safety improvements at FM 2001
  - Increase pedestrian connectivity between subdivisions and school
  - Aesthetic enhancements
- **Project was advertised for bid on November 7, 2018**
  - **Bid opening was held on December 11, 2018**
  - **Construction contract awarded to MA Smith Contracting Company**
  - **Notice to Proceed issued January 19, 2019**
  - **Road closed for Culvert 4 replacement on January 26th**
  - **Construction on-going**



### SAN ANTONIO ST./GARISON ROAD

The general scope of work for this project includes:

- Widening of existing pavement to enhance parking at Buda City Park
- Intersection safety improvements by separating San Antonio St. and Garison Road turning movements
- Aesthetic enhancements



**Construction was completed and road opened to traffic on November 20, 2018**




# BOND PROJECT UPDATES

## MAIN STREET IMPROVEMENTS

The general scope of work for this project includes:

- Widening of the Bradfield Drive / Main Street Intersection and extension of the 5 lane section to the west of Santa Cruz Catholic church
  - Signal Modification at Bradfield Drive and Main Street to accommodate additional lanes  
Bradfield Park cross culvert extension / modification
  - Extension of sidewalk along Main Street and improved accessibility to Bradfield Park
  - Select areas for pavement base repair
  - Pavement overlay and restriping
- 
- **Project is to be advertised for bid February 27, 2019**
  - **Bid opening scheduled for March 26th**
  - **Anticipated construction in late April 2019**
  - **The sequencing of the project has been adjusted to move the signalized intersection improvements at Main and Sequoyah/Loop Street up to the front of the project due to the increased traffic generated by the new municipal complex.**

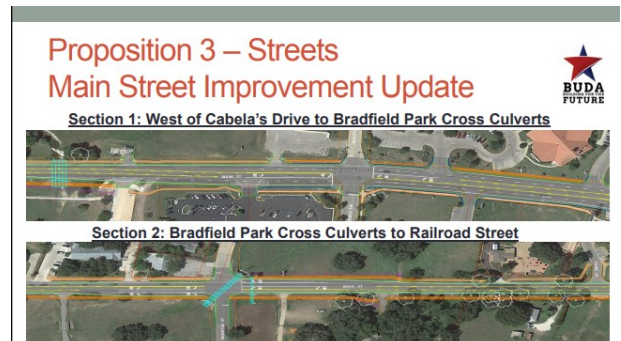

## MAIN STREET AT RM 967

The general scope of work for this project includes:

- Create turning lanes and through lanes to address traffic flow
  - Reconfiguration of sidewalks, signing and striping for enhanced pedestrian safety
  - Maintain existing diagonal parking
  - Relocation of traffic signal poles
- 
- **Project design is 95% complete**
  - **TxDOT anticipates project will go out to bid in late summer 2019**



## BOND PROJECT UPDATES

### RAINY DAY PROJECT — CABELA'S CONNECTOR

The general scope of work for this project includes:

- Development of a preliminary schematic including pavement design
- Geotechnical study, environmental study and utility conflict analysis
- Right of Way acquisition
- Project was submitted for potential CAMPO (Capital Area Metropolitan Planning Organization) funding under recent project call. Funding was not approved, but project ranked well
- Potential for funding to become available should other projects not utilize entire awarded funding
- Preliminary schematic is complete
- Geotechnical study and pavement design is complete
- Environmental study is complete
- City in discussions with property owner regarding right of entry and acquisition of right of way.

### PROPOSITION 4 DRAINAGE

#### PROJECT AREA 2 (Ongoing) HOUSTON STREET

Status:

- Construction Complete
- Substantial Completion Scheduled for March



#### PROJECT AREA 3 OXBOW NEIGHBORHOOD

Status:

- Construction Started in January
- Remuda Trail Culvert Structure Poured
- Relocation of Two PEC Power Poles in Progress





## BOND PROJECT UPDATES

### PROPOSITION 4 DRAINAGE

#### PROJECT AREA 1A FIRE STATION/BLUFF ST. (DIVERSION)

Status:

- 100% plans, specs, near final approval
- Advertise for bids May 2019

#### PROJECT AREA 1B W. GOFORTH

Status:

- 100% plans, specs, and estimate near final approval
- Advertise for bids September 2019

### PROPOSITION 5 PARKS AND TRAILS

#### CITY PARK

- City Park project was bid and the construction contract was awarded to the Barr Company in December 2018
- City Council voted to award construction of the full construction package including the amphitheater, stage, splash pad, and playgrounds
- Construction will begin in February 2019
- Construction anticipated February 2019 — January 2020

#### GREEN MEADOWS SPLASH PAD (COMPLETE)

- Splash Pad will open this spring
